




**CITY OF PLANO
COUNCIL AGENDA ITEM**


CITY SECRETARY'S USE ONLY				
<input type="checkbox"/> Consent <input type="checkbox"/> Regular <input type="checkbox"/> Statutory				
Council Meeting Date:		06/28/10		
Department:		Public Works & Engineering		
Department Head:		Alan L. Upchurch		
Agenda Coordinator (include phone #):		Irene Pegues (7198)		Project No. 5387
CAPTION				
To Tiseo Paving Company, increasing the contract by \$55,790 for McDermott Road from Ohio Drive to Coit Road, Change Order No. 2. Original Bid No. 2009-143-B.				
FINANCIAL SUMMARY				
<input type="checkbox"/> NOT APPLICABLE <input type="checkbox"/> OPERATING EXPENSE <input type="checkbox"/> REVENUE <input checked="" type="checkbox"/> CIP				
FISCAL YEAR: 2009-10	Prior Year (CIP Only)	Current Year	Future Years	TOTALS
Budget	34,513	3,140,487	0	3,175,000
Encumbered/Expended Amount	-34,513	-2,255,452	0	-2,289,965
This Item	0	-55,790	0	-55,790
BALANCE	0	829,245	0	829,245
FUND(S): STREET IMPROVEMENT CIP				
COMMENTS: Funds are included in the 2009-10 Street Improvement CIP. This item, in the amount of \$55,790, will leave a current year balance of \$829,245 for the McDermott – Coit to Ohio project. STRATEGIC PLAN GOAL: Contract modifications associated with street construction relate to the City's Goal of Financially Strong City with Service Excellence.				
SUMMARY OF ITEM				
This change order, in the amount of \$55,789.86, is for the adjustment in pay quantities to the amount actually installed, for issuing of revised construction plans for street lighting facilities and for the adjustment in pay items for the revised street lighting plans. The street light plans were required to be revised to avoid conflicts with the electrical transmission lines in the road median. Staff recommends approval of Change Order No. 2. The contract total will be \$2,224,614.21, which includes change orders of 4.33% of the original contract amount of \$2,132,270.05.				
List of Supporting Documents: Location Map; Change Order No. 2			Other Departments, Boards, Commissions or Agencies N/A	

McDERMOTT ROAD WIDENING FROM OHIO DRIVE TO COIT ROAD

PROJECT No. 5387

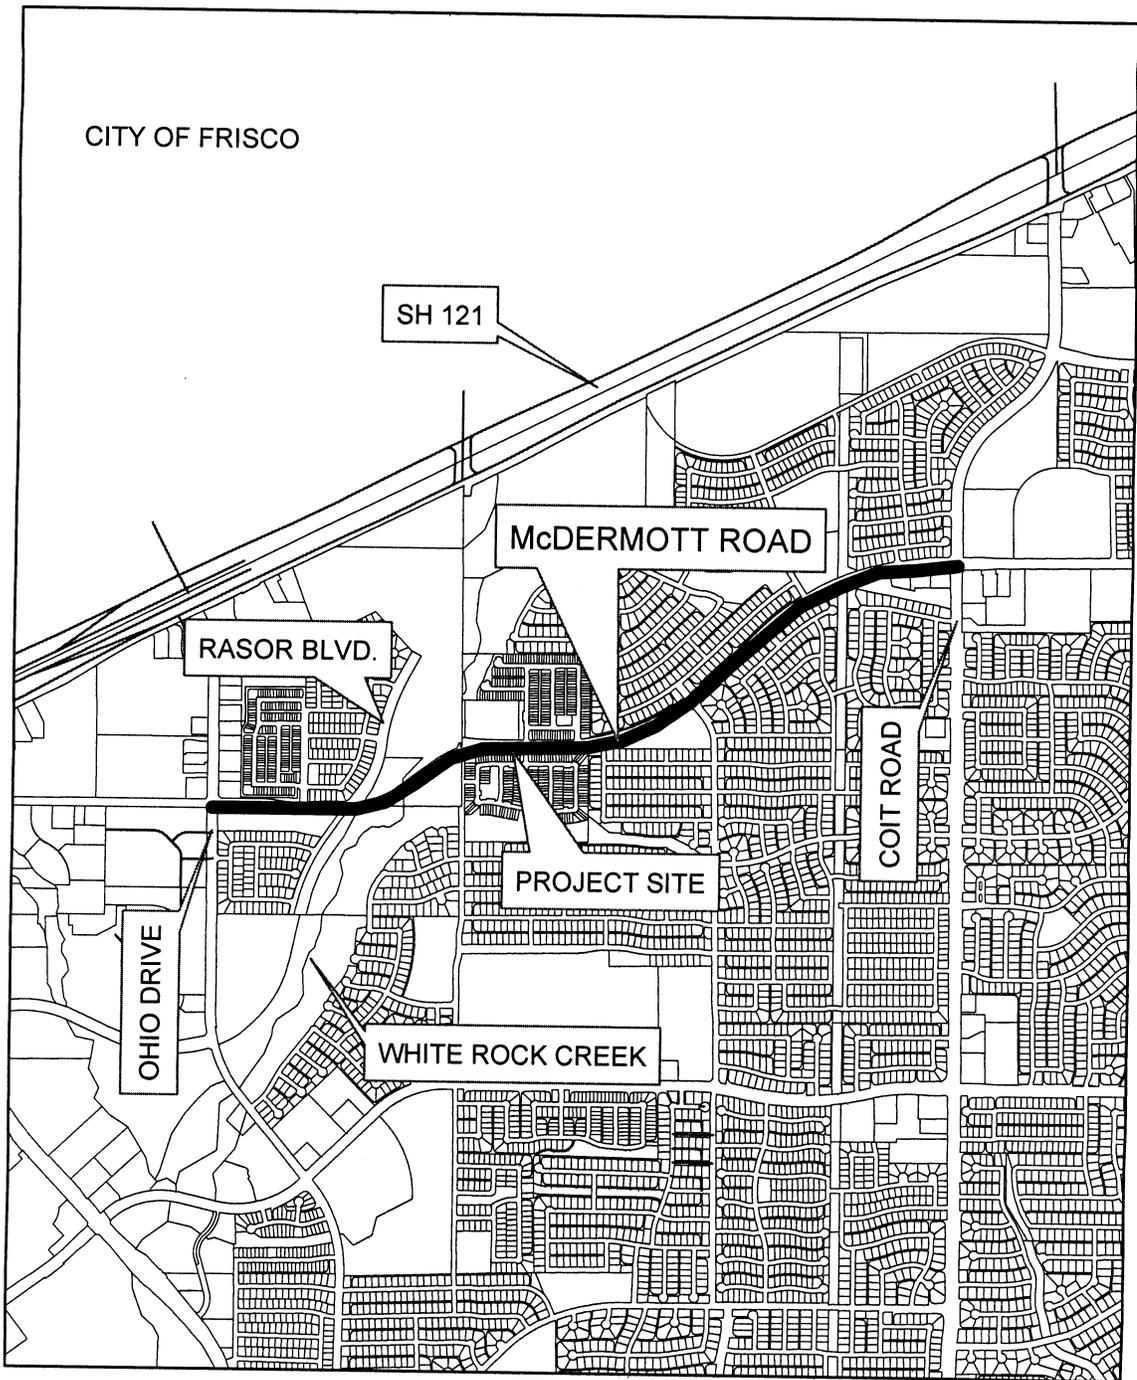

CITY OF PLANO
PUBLIC WORKS & ENGINEERING DEPT.



1 inch = 2,000 feet



CHANGE ORDER NO. 2

**MCDERMOTT ROAD FROM OHIO DRIVE TO COIT ROAD
PROJECT NO. 5387 (CSJ 0918-24-119)
PURCHASE ORDER NO. 103768
CIP NO. 31397
BID NO. 2009-143-B**

A. INTENT OF CHANGE ORDER

The intent of this change order is to modify the provisions of the contract entered into by the **CITY OF PLANO, TEXAS**, and **TISEO PAVING COMPANY** for the **MCDERMOTT ROAD OHIO DRIVE TO COIT ROAD PROJECT**, dated December 14, 2009.

B. DESCRIPTION OF CHANGE

The change order is for the adjustment of pay quantities to cover what is actually installed for the project, for the issuing of revised illumination conduit plans and the adjustment in pay items and quantities for the revised illumination plans.

C. EFFECT OF CHANGE

This change order will have the following effect on the cost of this project:

<i>ITEM NO.</i>	<i>ITEM DESCRIPTION</i>	<i>CURRENT QUANTITY</i>	<i>REVISED QUANTITY</i>	<i>UNIT</i>	<i>UNIT PRICE</i>	<i>AMOUNT OF CHANGE</i>
	FEDERAL PARTICIPATION					
23	Drill Shaft (30")	440	505.29	L.F.	\$124.00	\$8,095.96
60	Conc. Med. Mono Nose	22	67	S.Y.	\$75.00	\$3,375.00
91	Diodgrd Eros. Ctrl. Logs (12" Dia.)	2,976	3,276	L.F.	\$2.40	\$720.00
	SUB-TOTAL:					\$12,190.96
	CITY OF PLANO					
92	Condt (PVC)(SCHD 40)(2")	6,990	6,115	L.F.	\$4.30	-\$3,762.50
93	Condt (PVC)(SCHD 40)(2")(BORE)	845	1,181	L.F.	\$14.65	\$4,922.40
100	8" PVC DR-18 C900 Pipe	56	57	L.F.	\$75.00	\$75.00
101	6" PVC DR-14 C900 Pipe	24	26	L.F.	\$71.00	\$142.00
102	Adust Exist MH to Prop Grade	2	4	EA.	\$1,000.00	\$2,000.00
108	Condt (PVC)(SCHD 80)(2")	0	120	L.F.	\$6.85	\$822.00
109	Street Lt Base (OnCor)	0	18	EA.	\$1,200.00	\$21,600.00
110	Street Lt Base (CoServe)	0	8	EA.	\$1,400.00	\$11,200.00
111	Elect Pull Box (OnCor)	0	11	EA.	\$600.00	\$6,600.00
	SUB-TOTAL:					\$43,598.90
	TOTAL:					\$55,789.86

Original Contract Amount	<u>\$ 2,132,270.05</u>
Contract Amount (Including Previous Change Orders)	<u>\$ 2,168,824.35</u>
Amount, Change Order No. 2	<u>\$ 55,789.86</u>
Revised Contract Amount	<u>\$ 2,224,614.21</u>
Total Percent Increase Including Previous Change Orders	<u>4.33%</u>

D. EFFECT OF CHANGE ON CONTRACT TIME

The work required under this change order will add **20** day(s) to this project:

Original Contract Time	<u>200 working days</u>
Amount (Including Previous Change Orders)	<u>240 working days</u>
Amount, Change Order No. 2	<u>20 working days</u>
Revised Contract Time	<u>260 working days</u>
Total Percent Increase Including Previous Change Orders	<u>30.00%</u>

CONTINUED ON NEXT PAGE

E. AGREEMENT

By the signatures below, duly authorized agents of the **CITY OF PLANO, TEXAS**, and **TISEO PAVING COMPANY**, do hereby agree to append this Change Order No. 2 to the original contract between themselves, dated December 14, 2009.

**OWNER:
CITY OF PLANO**

**CONTRACTOR:
TISEO PAVING COMPANY**

By: _____
(signature)

By: _____
(signature)

Print
Name: Thomas H. Muehlenbeck

Print
Name: Robert Caudill

Print
Title: City Manager

Print
Title: Vice President

Date: _____

Date: _____

APPROVED AS TO FORM:

By: _____
Diane C. Wetherbee, City Attorney

ACKNOWLEDGMENTS

STATE OF TEXAS §
§
COUNTY OF DALLAS §

This instrument was acknowledged before me on the _____ day of _____, 2010, by **ROBERT CAUDILL, VICE PRESIDENT** of **TISEO PAVING COMPANY** a **TEXAS** corporation, on behalf of said corporation.

Notary Public, State of Texas

STATE OF TEXAS §
§
COUNTY OF COLLIN §

This instrument was acknowledged before me on the _____ day of _____, 2010, by **THOMAS H. MUEHLENBECK, CITY MANAGER** of the **CITY OF PLANO, TEXAS**, a Home-Rule Municipal Corporation, on behalf of said municipal corporation.

Notary Public, State of Texas
